

<b>Date Issued:</b>	4/13/2016	<b>Effective Date:</b>	
<b>Project:</b>	WTP Modifications	<b>Contract No.:</b>	2015-0062

<b>Owner:</b>	City of Franklin	<b>Owner's Project No.:</b>	2015-0062
<b>Engineer:</b>	Smith Seckman Reid, Inc.	<b>SSR Project No.:</b>	12-41-013.0
<b>Contractor:</b>	Judy Construction Co.	<b>Government Project No.:</b>	N/A

The contractor is hereby authorized and directed to make the changes described below, and agrees to furnish all labor, materials, and equipment to accomplish the changes in accordance with the applicable portions of the Contract Documents for this project.

**Description of Change (Including Location and Reasons Therefore):**

See attached "Change Control Forms."

In executing this change order, it is mutually agreed that the amounts provided for herein will be accepted by the contractor as full compensation for all known costs associated in the work, including all direct and indirect costs, and any and all known costs associated with delays or additional time, if any, which may be required as a result of said changes.

	AMOUNT		CONTRACT TIME
Original Contract Price	\$14,018,000.00	Substantial Completion Date Prior to Change Order	10/25/2017
Contract Price Prior to Change Order	\$14,018,000.00	Final Payment Date Prior To Change Order	11/24/2017
Net Amount This Change Order	-\$171,937.53	Net Time This Change Order	56 days
Revised Contract Price	\$13,846,062.47	Revised Substantial Completion Date	12/20/2017
		Revised Final Payment Date	1/19/2018

Recommended By:

  
\_\_\_\_\_  
Engineer

4/13/2016

\_\_\_\_\_  
Date

Accepted By:

  
\_\_\_\_\_  
Contractor

4/13/2016

\_\_\_\_\_  
Date

Approved By:

\_\_\_\_\_  
Owner

\_\_\_\_\_  
Date

SMITH SECKMAN REID, INC.  
 2995 Sidco Drive  
 Nashville, TN  
 PHONE: (615) 383-1113 | FAX: (615) 386-8469



CCF# **001**  
 Date Issued: **9/23/15**

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>
Engineer:	<b>Smith Seckman Reid, Inc.</b>
Contractor:	<b>Judy Construction Company</b>

**DESCRIPTION OF CHANGE**

Supplier of Granular Activated Carbon Pressure Contactors shall be Calgon Carbon Corporation.

(Attach Supporting Documentation)

Requested By:	<b>OWNER</b>
This Document is a:	<b>CONTRACTOR CHANGE REQUEST</b>
Drawing(s) Reference:	<b>n/a</b>
Spec. Reference:	<b>46 61 21</b>

**REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM**

We propose to perform the Work or make the Claim described above for the following change in Contract

Cost and Contract Times:

- |   |  |               |
|---|--|---------------|
| <input checked="" type="checkbox"/> No Change in Contract Amount is required. | <input type="checkbox"/> A Change in Contract Amount is required:<br>Add/Deduct (Circle One) | <b>\$0.00</b> |
| <input checked="" type="checkbox"/> No Change in Contract Time is required.   | <input type="checkbox"/> A Change in Contract Time is required:                              | days          |

Engineer:	<u>Joseph Duffey</u> (Authorized Signature)	Contractor:	<u>John Whalen</u> (Authorized Signature)
Owner:	<u>[Signature]</u> (Authorized Signature)	<input checked="" type="checkbox"/> Recommends Acceptance	<input type="checkbox"/> Recommends Rejection

**WORK CHANGE DIRECTIVE**

You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.

Recommended by Engineer:	Date:
Authorized by Owner:	Date:
Accepted by Contractor:	Date:

**FIELD ORDER**

This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.




Recommended by RPR:	Date:
Directed by Engineer:	Date:
Accepted by Contractor:	Date:

SMITH SECKMAN REID, INC.  
 2995 Sidco Drive  
 Nashville, TN  
 PHONE: (615) 383-1113 | FAX: (615) 386-8469



CCF# **002**  
 Date Issued: **9/23/15**

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>		
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>		
Engineer:	<b>Smith Seckman Reid, Inc.</b>		
Contractor:	<b>Judy Construction Company</b>		
<b>DESCRIPTION OF CHANGE</b>			
Owner elects to utilize Jim Myers & Sons, Inc. as supplier of Sludge Collectors.			
(Attach Supporting Documentation)			
Requested By:	<b>OWNER</b>		
This Document is a:	<b>CONTRACTOR CHANGE REQUEST</b>		
Drawing(s) Reference:	<b>n/a</b>	Spec. Reference:	<b>46 43 79</b>
<b>REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM</b>			
We propose to perform the Work or make the Claim described above for the following change in Contract			
<b>Cost and Contract Times:</b>			
<input type="checkbox"/>	No Change in Contract Amount is required.	<input checked="" type="checkbox"/>	A Change in Contract Amount is required: Deduct <b>\$60,000.00</b>
<input checked="" type="checkbox"/>	No Change in Contract Time is required.	<input type="checkbox"/>	A Change in Contract Time is required: _____ <b>days</b>
Engineer:	 (Authorized Signature)	Contractor:	 (Authorized Signature)
Owner:	 (Authorized Signature)	<input checked="" type="checkbox"/>	Recommends Acceptance
		<input type="checkbox"/>	Recommends Rejection
<b>WORK CHANGE DIRECTIVE</b>			
You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.			
Recommended by Engineer:		Date:	
Authorized by Owner:		Date:	
Accepted by Contractor:		Date:	
<b>FIELD ORDER</b>			
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.			
Recommended by RPR:		Date:	
Directed by Engineer:		Date:	
Accepted by Contractor:		Date:	

### CHANGE CONTROL FORM (CCF)

Owner Contract No.	<b>2015-0062</b>
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>
Engineer:	<b>Smith Seckman Reid, Inc.</b>
Contractor:	<b>Judy Construction Company</b>

#### DESCRIPTION OF CHANGE

Owner elects to remove Facility Online Training, Section 01 79 00.



(Attach Supporting Documentation)

Requested By:	<b>OWNER</b>		
This Document is a:	<b>CONTRACTOR CHANGE REQUEST</b>		
Drawing(s) Reference:	<b>None</b>	Spec. Reference:	<b>01 79 00</b>

#### REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM

We propose to perform the Work or make the Claim described above for the following change in Contract  
**Cost and Contract Times:**

- |   |   |
|---|---|
| <input type="checkbox"/> No Change in Contract Amount is required.          | <input checked="" type="checkbox"/> A Change in Contract Amount is required: Deduct <b>\$119,275.00</b> |
| <input checked="" type="checkbox"/> No Change in Contract Time is required. | <input type="checkbox"/> A Change in Contract Time is required: _____ days                              |

Engineer: <u></u> <small>(Authorized Signature)</small>	Contractor: <u></u> <small>(Authorized Signature)</small>
Owner: <u></u> <small>(Authorized Signature)</small>	<input checked="" type="checkbox"/> Recommends Acceptance <input type="checkbox"/> Recommends Rejection

#### WORK CHANGE DIRECTIVE

You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.




Recommended by Engineer:	Date:
Authorized by Owner:	Date:
Accepted by Contractor:	Date:

#### FIELD ORDER

This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.

Recommended by RPR:	Date:
Directed by Engineer:	Date:
Accepted by Contractor:	Date:

### CHANGE CONTROL FORM (CCF)

Owner Contract No.	<b>2015-0062</b>		
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>		
Engineer:	<b>Smith Seckman Reid, Inc.</b>		
Contractor:	<b>Judy Construction Company</b>		
<b>DESCRIPTION OF CHANGE</b>			
Credit to Owner for unused portion of Utility Relocation Cash Allowance.			
(Attach Supporting Documentation)			
Requested By:	<b>ENGINEER</b>		
This Document is a:	<b>REQUEST FOR PROPOSAL (RFP)</b>		
Drawing(s) Reference:	<b>None</b>	Spec. Reference:	<b>01 21 00</b>
<b>REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM</b>			
We propose to perform the Work or make the Claim described above for the following change in Contract			
<b>Cost and Contract Times:</b>			
<input type="checkbox"/> No Change in Contract Amount is required.	<input checked="" type="checkbox"/> A Change in Contract Amount is required: Deduct	<b>\$836.55</b>	
<input checked="" type="checkbox"/> No Change in Contract Time is required.	<input type="checkbox"/> A Change in Contract Time is required:	days	
Engineer:	 (Authorized Signature)	Contractor:	 (Authorized Signature)
Owner:	 (Authorized Signature)	<input checked="" type="checkbox"/> Recommends Acceptance	
<input type="checkbox"/> Recommends Rejection			
<b>WORK CHANGE DIRECTIVE</b>			
You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.			
Recommended by Engineer:		Date:	
Authorized by Owner:		Date:	
Accepted by Contractor:		Date:	
<b>FIELD ORDER</b>			
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.			
Recommended by RPR:		Date:	
Directed by Engineer:		Date:	
Accepted by Contractor:		Date:	

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>
Engineer:	<b>Smith Seckman Reid, Inc.</b>
Contractor:	<b>Judy Construction Company</b>

**DESCRIPTION OF CHANGE**

Cost of AT&T relocation work.

(Attach Supporting Documentation)




Requested By:	<b>ENGINEER</b>		
This Document is a:	<b>REQUEST FOR PROPOSAL (RFP)</b>		
Drawing(s) Reference:	<b>None</b>	Spec. Reference:	<b>None</b>

**REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM**

We propose to perform the Work or make the Claim described above for the following change in Contract

Cost and Contract Times:

<input type="checkbox"/> No Change in Contract Amount is required.	<input checked="" type="checkbox"/> A Change in Contract Amount is required: Add	<b>\$2,639.02</b>
<input checked="" type="checkbox"/> No Change in Contract Time is required.	<input type="checkbox"/> A Change in Contract Time is required:	days

Engineer:	 (Authorized Signature)	Contractor:	 (Authorized Signature)
Owner:	 (Authorized Signature)	<input checked="" type="checkbox"/> Recommends Acceptance	<input type="checkbox"/> Recommends Rejection

**WORK CHANGE DIRECTIVE**

You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.




Recommended by Engineer:	Date:
Authorized by Owner:	Date:
Accepted by Contractor:	Date:

**FIELD ORDER**

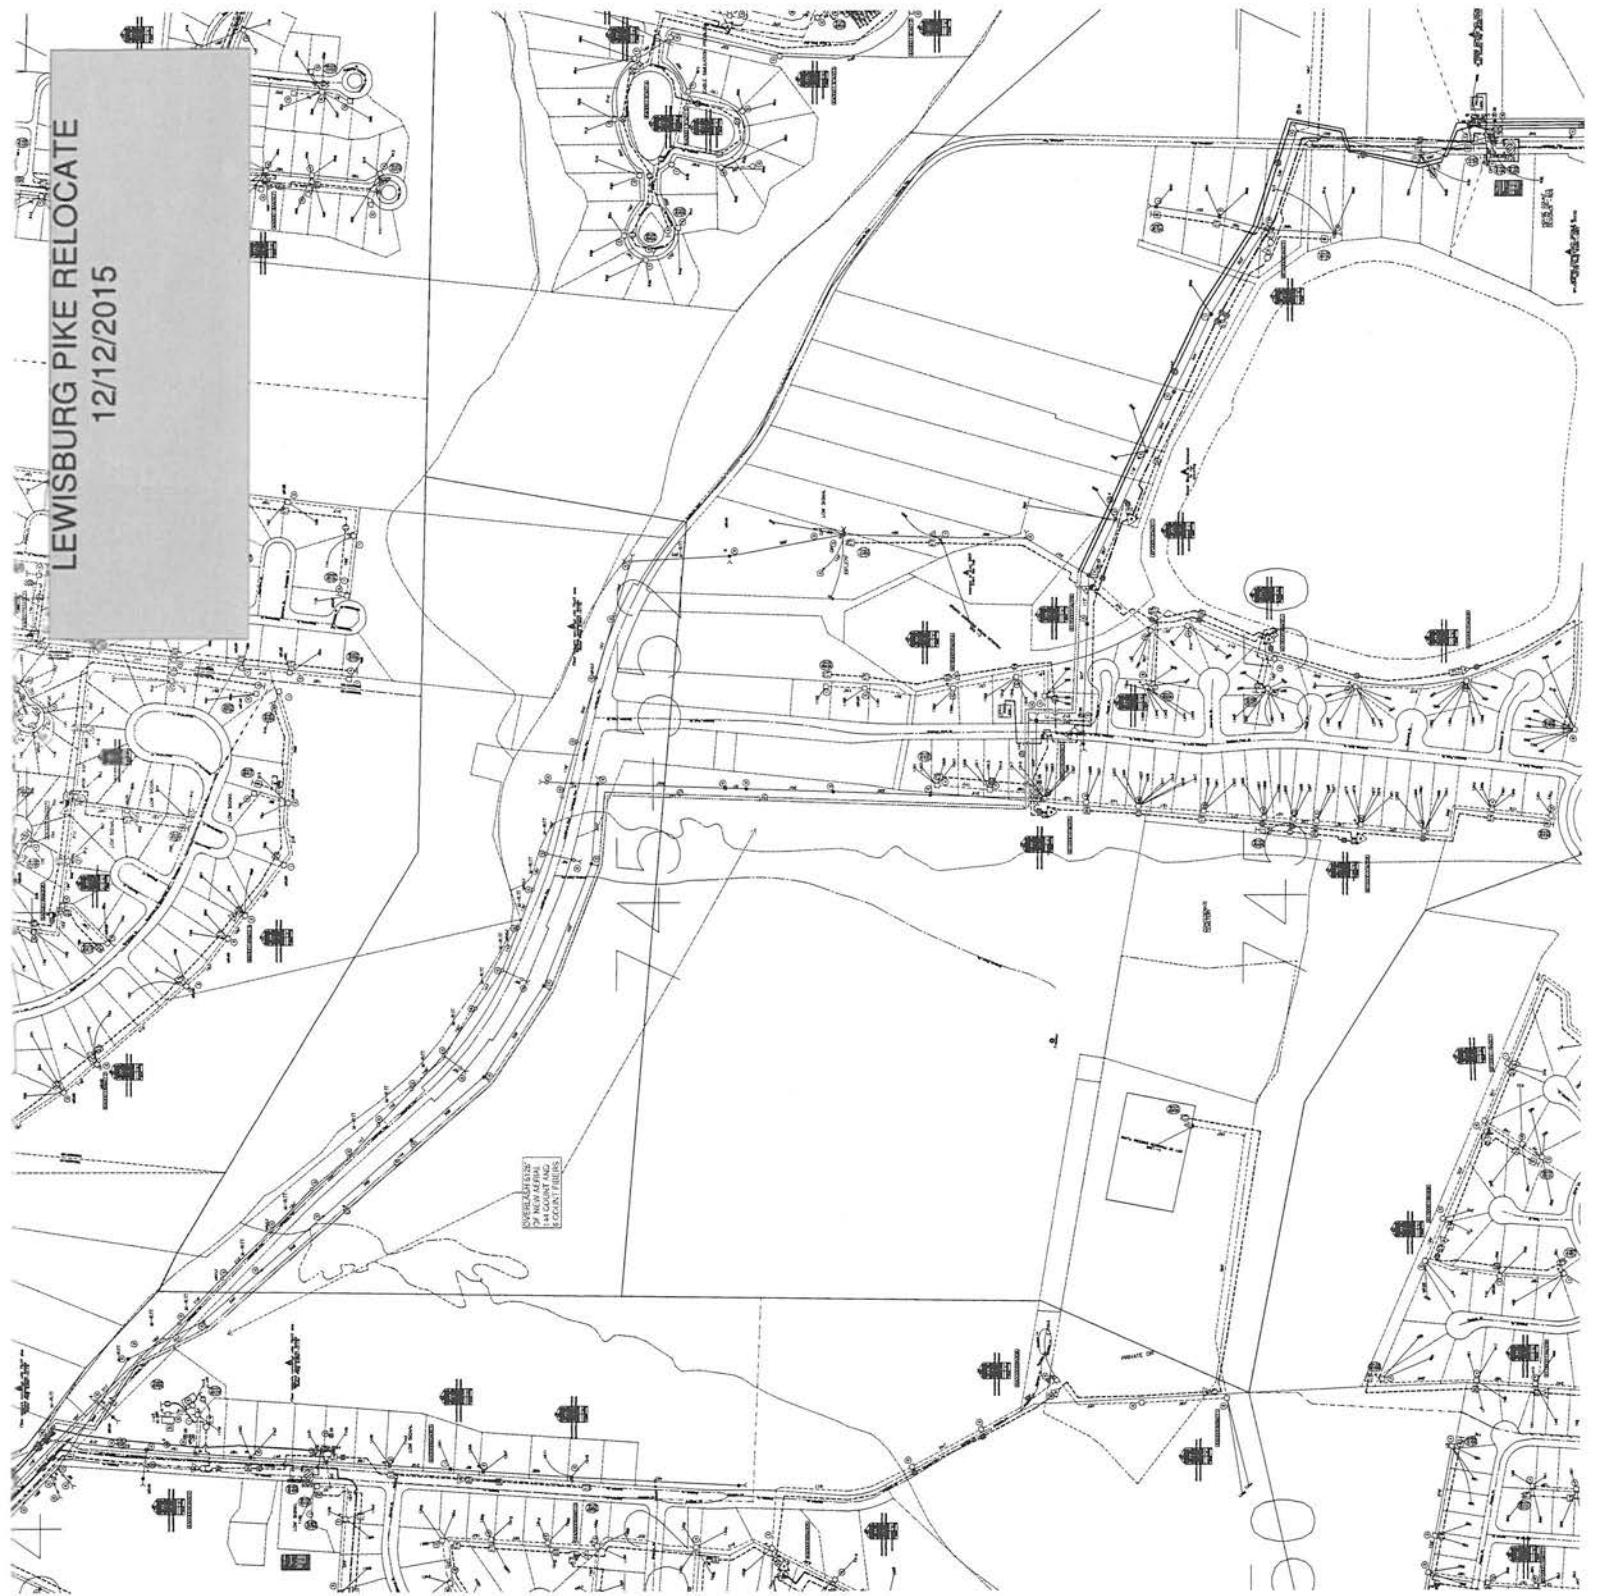
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.

Recommended by RPR:	Date:
Directed by Engineer:	Date:
Accepted by Contractor:	Date:

**CHANGE CONTROL FORM (CCF)**

Owner Contract No. <b>2015-0062</b>	
Project Name: <b>Franklin Water Treatment Plant Modifications</b>	
Engineer: <b>Smith Seckman Reid, Inc.</b>	
Contractor: <b>Judy Construction Company</b>	
<b>DESCRIPTION OF CHANGE</b>	
Time extension associated with delays in relocating existing utilities in conflict with proposed work. Recommendation on Contractor request for General Conditions cost adjustment associated with these delays as outlined in the attached letter is deferred until a date closer to Substantial Completion.	
(Attach Supporting Documentation)	
Requested By: <b>CONTRACTOR</b>	
This Document is a: <b>CONTRACTOR CHANGE REQUEST</b>	
Drawing(s) Reference: <b>None</b>	Spec. Reference: <b>None</b>
<b>REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM</b>	
We propose to perform the Work or make the Claim described above for the following change in Contract Cost and Contract Times:	
<input type="checkbox"/> No Change in Contract Amount is required.	<input type="checkbox"/> A Change in Contract Amount is required:
<input type="checkbox"/> No Change in Contract Time is required.	<input checked="" type="checkbox"/> A Change in Contract Time is required: <b>56 days</b>
Engineer: <u></u> (Authorized Signature)	Contractor: <u></u> (Authorized Signature)
Owner: <u></u> (Authorized Signature)	<input checked="" type="checkbox"/> Recommends Acceptance <input type="checkbox"/> Recommends Rejection
<b>WORK CHANGE DIRECTIVE</b>	
You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.	
Recommended by Engineer:	Date:
Authorized by Owner:	Date:
Accepted by Contractor:	Date:
<b>FIELD ORDER</b>	
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.	
Recommended by RPR:	Date:
Directed by Engineer:	Date:
Accepted by Contractor:	Date:

LEWISBURG PIKE RELOCATE  
12/12/2015



CONSTRUCTION  
OF NEW ASPHALT  
PAVEMENT





P.O. BOX 457 CYNTHIANA, KENTUCKY 41031  
Telephone (859) 234-6900 Fax (859) 234-3480  
www.judyconstructionco.com

March 21, 2016

Smith Seckman Reid, Inc.  
2995 Sidco Drive  
Nashville, TN 37204  
Attn: Andrew Johnson

**Ref: City of Franklin, Tennessee  
Water Treatment Plant Modifications (COF No. 2015-0062)  
Construction Delays**

Dear Andrew,

This letter is to follow-up to our previous correspondence concerning delays to the project construction schedule and to formally request a time extension.

The relocation of the utility lines has been the biggest problem and is the source of most of the delay. Judy Construction Company, Smith Seckman Reid, and the City of Franklin have all worked diligently to relocate the utility lines as quickly as possible; the topic was first discussed at the Pre-Construction Conference. MTEMC was able to remove the power lines on December 22, 2015; nearly two months after the Notice to Proceed. Comcast removed their line 130 days after the NTP on March 4, 2016. We were able to work during this time however we were not always working on critical path items and critical work took longer than it should have (attempting to work below or near utility lines). When reviewing the work completed to date, it's apparent the relocation of the utility lines should add 7 weeks to the duration of the project.

Unfortunately the delays caused by the utility line relocation have also been detrimental to Judy Construction Company in terms of cost. Our monthly operating expense is high and occurs whether or not we're making progress. These costs include supervision, supervision insurance, travel expenses, pickup truck, etc. Please consider reimbursing us for a portion of our losses. We're asking to be reimbursed for 5 weeks out of the 7 weeks lost. Out of those 5 weeks, we're only requesting a portion of our cost per week. We request \$13,035 to be included for General Condition cost towards the time extension Change Order.

The replacement of the waste line (CCF 011) is another item that caused significant delay to the project. The existing line had deteriorated, requiring replacement and not all lines were correctly shown on the contract drawings. It took more than six weeks to evaluate the best




*Celebrating 40 Years of Business*



plan for replacement, estimate the cost for approval, and receive the required materials. Replacement of the waste line requires at least one week added to the contract.

To conclude, we request at least 8 weeks (56 days) be added to the contract time to cover the delays noted above. We're also hopeful to recover a portion of our losses due to the delays in the amount listed above. Please review and let us know if you agree. If you have any questions please do not hesitate to contact me.

Sincerely,

A handwritten signature in black ink, appearing to read "John Whalen II". The signature is fluid and cursive, with a long horizontal stroke at the end.

John F. Whalen II  
Project Manager




cc: Steve Judy  
Ben Williams  
Macy Gibson

SMITH SECKMAN REID, INC.  
 2995 Sidco Drive  
 Nashville, TN  
 Phone: (615) 383-1113 | Fax: (615) 386-8469






CCF# **008**  
 Date Issued: **12/7/15**

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>		
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>		
Engineer:	<b>Smith Seckman Reid, Inc.</b>		
Contractor:	<b>Judy Construction Company</b>		
<b>DESCRIPTION OF CHANGE</b>			
Clarification for the connection of the feeders to the motor leads of the Raw Water Pumps.			
(Attach Supporting Documentation)			
Requested By:	<b>ENGINEER</b>		
This Document is a:	<b>REQUEST FOR PROPOSAL (RFP)</b>		
Drawing(s) Reference:	<b>ES1.0, E6.1</b>	Spec. Reference:	<b>NA</b>
<b>REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM</b>			
We propose to perform the Work or make the Claim described above for the following change in Contract Cost and Contract Times:			
<input checked="" type="checkbox"/>	No Change in Contract Amount is required.	<input type="checkbox"/>	A Change in Contract Amount is required:
<input checked="" type="checkbox"/>	No Change in Contract Time is required.	<input type="checkbox"/>	A Change in Contract Time is required: _____ days
Engineer:	 (Authorized Signature)	Contractor:	 (Authorized Signature)
Owner:	 (Authorized Signature)	<input checked="" type="checkbox"/>	Recommends Acceptance
		<input type="checkbox"/>	Recommends Rejection
<b>WORK CHANGE DIRECTIVE</b>			
You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.			
Recommended by Engineer:		Date:	
Authorized by Owner:		Date:	
Accepted by Contractor:		Date:	
<b>FIELD ORDER</b>			
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.			
Recommended by RPR:		Date:	
Directed by Engineer:		Date:	
Accepted by Contractor:		Date:	

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>		
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>		
Engineer:	<b>Smith Seckman Reid, Inc.</b>		
Contractor:	<b>Judy Construction Company</b>		
<b>DESCRIPTION OF CHANGE</b>			
Relocate the existing MCC that services the existing High Service Pumps.			
(Attach Supporting Documentation)			
Requested By:	<b>CONTRACTOR</b>		
This Document is a:	<b>CONTRACTOR CHANGE REQUEST</b>		
Drawing(s) Reference:	<b>ES1.0, CS2.2</b>	Spec. Reference:	<b>None</b>
<b>REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM</b>			
We propose to perform the Work or make the Claim described above for the following change in Contract			
<b>Cost and Contract Times:</b>			
<input type="checkbox"/>	No Change in Contract Amount is required.	<input checked="" type="checkbox"/>	A Change in Contract Amount is required: <b>Add</b> <span style="float:right;"><b>\$3,117.00</b></span>
<input checked="" type="checkbox"/>	No Change in Contract Time is required.	<input type="checkbox"/>	A Change in Contract Time is required: <span style="float:right;">days</span>
Engineer:	 (Authorized Signature)	Contractor:	 (Authorized Signature)
Owner:	 (Authorized Signature)	<input checked="" type="checkbox"/>	Recommends Acceptance
		<input type="checkbox"/>	Recommends Rejection
<b>WORK CHANGE DIRECTIVE</b>			
You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.			
Recommended by Engineer:		Date:	
Authorized by Owner:		Date:	
Accepted by Contractor:		Date:	
<b>FIELD ORDER</b>			
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.			
Recommended by RPR:		Date:	
Directed by Engineer:		Date:	
Accepted by Contractor:		Date:	

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>
Engineer:	<b>Smith Seckman Reid, Inc.</b>
Contractor:	<b>Judy Construction Company</b>

**DESCRIPTION OF CHANGE**

Additional tree removal and trimming required to accommodate the new entrance road. Includes removing and reinstalling the tree protection fence. Includes hauling away debris that can not be chipped.




(Attach Supporting Documentation)

Requested By:	<b>CONTRACTOR</b>		
This Document is a:	<b>CONTRACTOR CHANGE REQUEST</b>		
Drawing(s) Reference:	<b>CG1.1</b>	Spec. Reference:	<b>None</b>

**REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM**

We propose to perform the Work or make the Claim described above for the following change in Contract  
**Cost and Contract Times:**

<input type="checkbox"/> No Change in Contract Amount is required.	<input checked="" type="checkbox"/> A Change in Contract Amount is required: Add	<b>\$2,418.00</b>
<input checked="" type="checkbox"/> No Change in Contract Time is required.	<input type="checkbox"/> A Change in Contract Time is required:	days

Engineer:	 (Authorized Signature)	Contractor:	 (Authorized Signature)
Owner:	 (Authorized Signature)	<input checked="" type="checkbox"/> Recommends Acceptance	<input type="checkbox"/> Recommends Rejection

**WORK CHANGE DIRECTIVE**

You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.

Recommended by Engineer:	Date:
Authorized by Owner:	Date:
Accepted by Contractor:	Date:

**FIELD ORDER**

This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.

Recommended by RPR:	Date:
Directed by Engineer:	Date:
Accepted by Contractor:	Date:

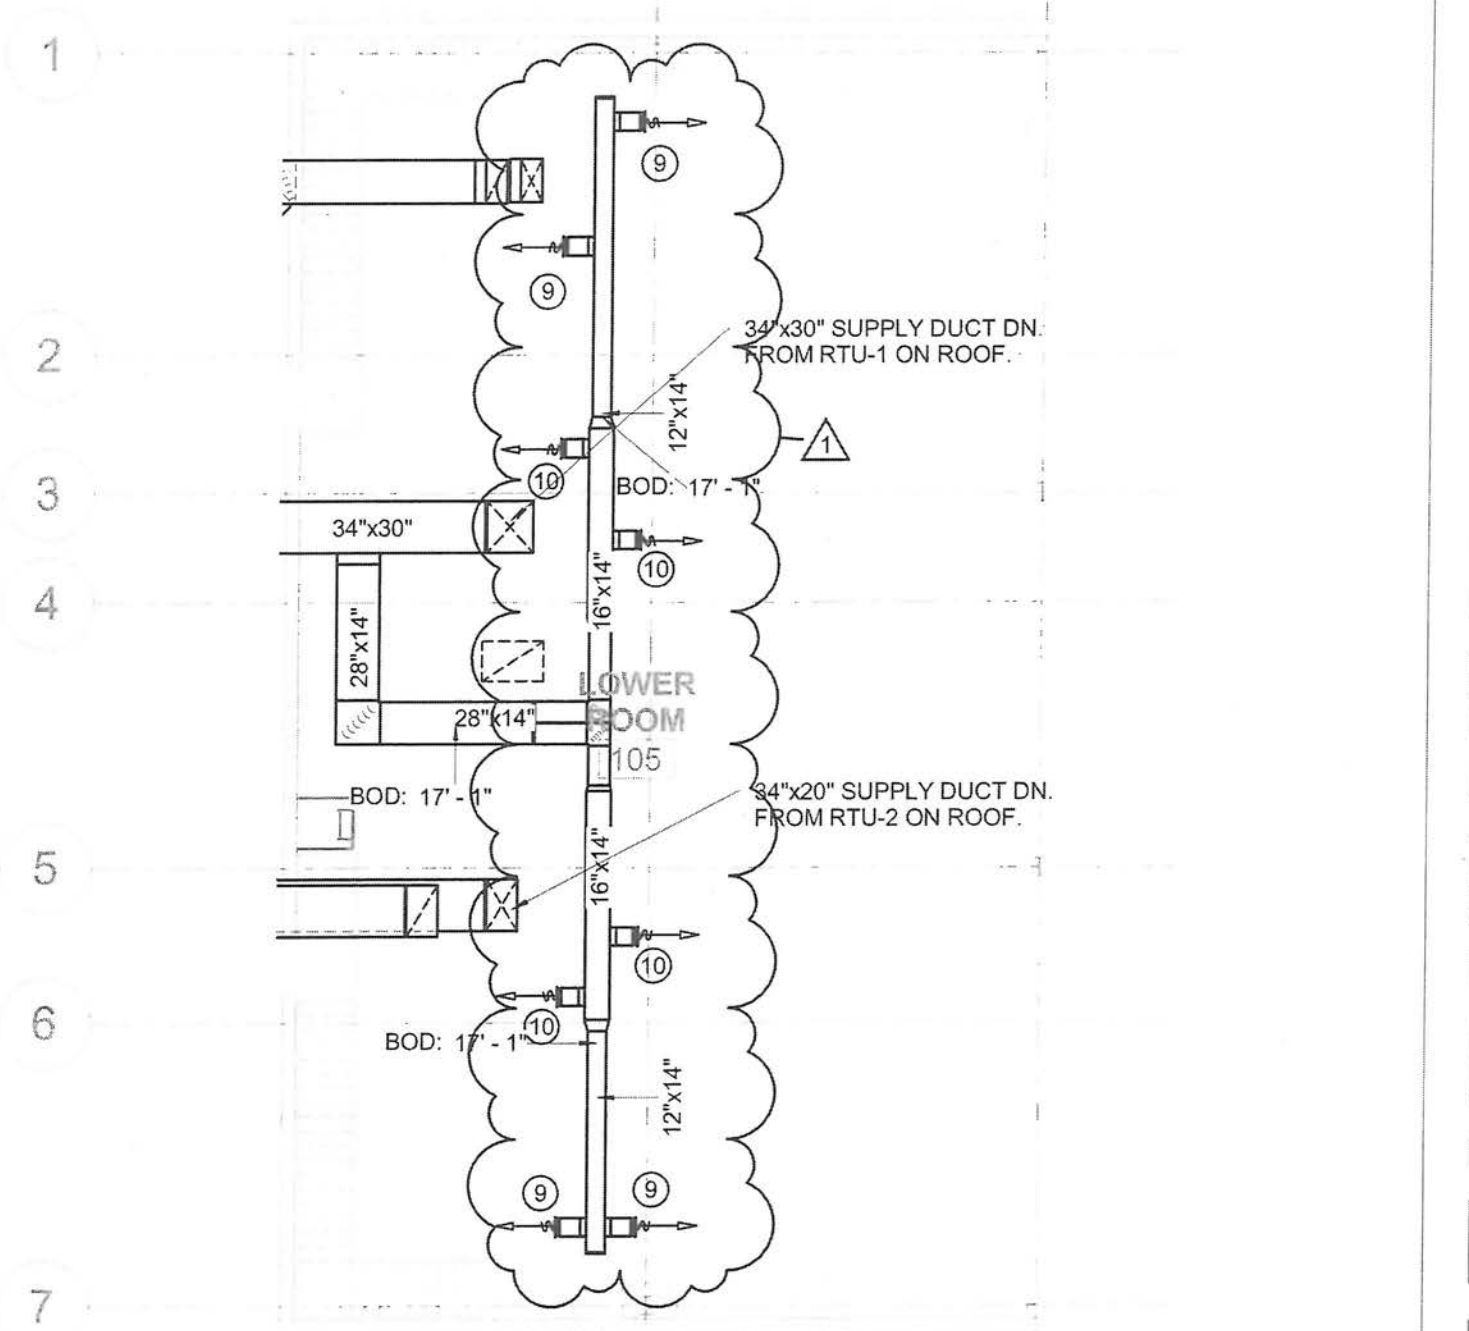
SMITH SECKMAN REID, INC.  
 2995 Sidco Drive  
 Nashville, TN  
 PHONE: (615) 383-1113 | FAX: (615) 386-8469



CCF# **012**  
 Date Issued: **1/6/16**

**CHANGE CONTROL FORM (CCF)**

Owner Contract No.	<b>2015-0062</b>		
Project Name:	<b>Franklin Water Treatment Plant Modifications</b>		
Engineer:	<b>Smith Seckman Reid, Inc.</b>		
Contractor:	<b>Judy Construction Company</b>		
<b>DESCRIPTION OF CHANGE</b>			
Duct relocation in GAC Room, Rm. 105. Ducts moved to avoid conflict with height of GAC tanks. See attached Sketch SKM-1 for details.			
(Attach Supporting Documentation)			
Requested By:	<b>ENGINEER</b>		
This Document is a:	<b>FIELD ORDER (FO)</b>		
Drawing(s) Reference:	<b>M1.1-07</b>	Spec. Reference:	<b>N/A</b>
<b>REQUEST FOR PROPOSAL / CHANGE REQUEST / CLAIM</b>			
We propose to perform the Work or make the Claim described above for the following change in Contract			
<b>Cost and Contract Times:</b>			
<input type="checkbox"/> No Change in Contract Amount is required.	<input type="checkbox"/> A Change in Contract Amount is required: Add/Ded		
<input type="checkbox"/> No Change in Contract Time is required.	<input type="checkbox"/> A Change in Contract Time is required:		days
Engineer: _____	Contractor: _____		
(Authorized Signature)	(Authorized Signature)		
Owner: _____	<input checked="" type="checkbox"/> Recommends Acceptance		
(Authorized Signature)	<input type="checkbox"/> Recommends Rejection		
<b>WORK CHANGE DIRECTIVE</b>			
You are directed to proceed to make the changes to the Work described in this Work Change Directive. Any change in Contract Price or Contract Time will be determined in accordance with the General Conditions.			
Recommended by Engineer:			Date: _____
Authorized by Owner:			Date: _____
Accepted by Contractor:			Date: _____
<b>FIELD ORDER</b>			
This Field Order issued in accordance with the General Conditions for minor changes in the Work without changes in the Contract Price or Contract Time. If you consider that a change in Contract Price or Contract Times is required, notify the Resident Project Representative immediately and before proceeding with the Work.			
Recommended by RPR: _____	Date: <b>1/18/2016</b>		
Directed by Engineer: _____	Date: <b>1/6/2016</b>		
Accepted by Contractor: _____	Date: <b>1/18/16</b>		



① UPPER LEVEL - MECHANICAL DUCTWORK PARTIAL PLAN  
 1" = 10'-0"

**SSR** Smith  
 Seckman  
 Reid, Inc.

2995 Sidco Drive  
 Nashville, TN 37204  
 (615) 383-1113  
 FAX: (615) 386-8469  
 www.ssr-inc.com

DATE: 01/06/16  
 REF. SHT M1.1-07

THE CITY OF FRANKLIN, TENNESSEE  
 WATER TREATMENT PLANT  
 FIELD ORDER REVISION

**SKM-1**
